

Massachusetts Department of Transportation
608164 - Town of Sudbury, MA - Bruce Freeman Rail Trail
UD PDS Schedule

WBS	ID	Name	Start	Finish	Duration	Actual Duration	Remaining Duration	Responsibility	Total Slack	Act. Start	Act. Finish	% Complete	Timeline											
													1st Quarter	3rd Quarter	1st Quarter	3rd Quarter	1st Quarter	3rd Quarter	1st Quarter	3rd Quarter	1st Quarter	3rd Quarter	1st Quarter	3rd Quarter
CNT	1	Contract/Project Management	Wed 1/2/19	Sun 8/11/24	2049d	0d	2049d		0d	NA	NA	0%	Contract/Project Management											
CNT.MS	2	Project Milestones	Wed 1/2/19	Sun 8/11/24	2049d	0d	2049d		0d	NA	NA	0%	Project Milestones											
CNT.MS.010	3	Issue Design Contract NTP	Wed 1/2/19	Wed 1/2/19	0d	0d	0d	MassDOT.PM	731.8d	NA	NA	0%	◆ Issue Design Contract NTP											
CNT.MS.020	4	PM Submits Documents for Advertising	Mon 4/11/22	Mon 4/11/22	1d	0d	1d	MassDOT.PM	0d	NA	NA	0%												
CNT.MS.030	5	Submit Mylar Title Sheet and CDs	Mon 4/11/22	Mon 4/11/22	0d	0d	0d	Consultants.DES	428d	NA	NA	0%												
CNT.MS.040	6	Prepare for Advertise	Tue 4/12/22	Fri 4/22/22	11d	0d	11d	MassDOT.FAPO	0d	NA	NA	0%												
CNT.MS.050	7	Advertise Construction Contract	Sat 4/23/22	Sat 4/23/22	1d	0d	1d	MassDOT.PM	0d	NA	NA	0%												
CNT.MS.060	8	Bid Opening	Tue 6/13/23	Tue 6/13/23	0d	0d	0d	MassDOT.PM	0d	NA	NA	0%												
CNT.MS.070	9	Issue Construction Contract NTP	Sat 8/12/23	Sat 8/12/23	0d	0d	0d	MassDOT.PM	0d	NA	NA	0%												
CNT.MS.080	10	Scope of Service Complete	Sun 8/11/24	Sun 8/11/24	0d	0d	0d	MassDOT.PM	0d	NA	NA	0%												
CNT.100	11	Project Development	Wed 1/2/19	Sun 1/26/20	390d	0d	390d		1659d	NA	NA	0%	Project Development											
CNT.100.010	12	Finalize Project Plan and Design Schedule	Wed 1/2/19	Thu 1/31/19	30d	0d	30d	Consultants.DES	1659d	NA	NA	0%												
CNT.100.020	13	Project Design Schedule Updates	Fri 2/1/19	Sun 1/26/20	360d	0d	360d	Consultants.DES	1659d	NA	NA	0%												
HWY	14	Highway Design	Sun 3/24/19	Wed 12/15/21	997d	427.53d	569.47d		970d	Sun 3/24/19	NA	43%	Highway Design											
HWY.200	15	Functional Design Report	Thu 1/28/21	Sat 6/26/21	150d	0d	150d		1142d	NA	NA	0%	Functional Design Report											
HWY.200.010	16	Prepare Functional Design Report	Thu 1/28/21	Sun 3/28/21	60d	0d	60d	Consultants.DES	1142d	NA	NA	0%												
HWY.200.020	17	Submit Functional Design Report	Sun 3/28/21	Sun 3/28/21	0d	0d	0d	Consultants.DES	1142d	NA	NA	0%												
HWY.200.030	18	Review Functional Design Report	Mon 3/29/21	Sat 6/26/21	90d	0d	90d	MassDOT.HW	1142d	NA	NA	0%												
HWY.200.040	19	Approval of Functional Design Report	Sat 6/26/21	Sat 6/26/21	0d	0d	0d	MassDOT.HW	1142d	NA	NA	0%												
HWY.220	20	Design Justification Workbook	Thu 1/28/21	Sun 3/28/21	60d	0d	60d		1232d	NA	NA	0%	Design Justification Workbook											
HWY.220.010	21	Prepare Design Exception Report	Thu 1/28/21	Sun 3/28/21	60d	0d	60d	Consultants.DES	1232d	NA	NA	0%												
HWY.220.020	22	Submit Design Exception Report	Thu 1/28/21	Thu 1/28/21	0d	0d	0d	Consultants.DES	1232d	NA	NA	0%												
HWY.220.030	23	Review Design Exception Report	Thu 1/28/21	Fri 2/26/21	30d	0d	30d	MassDOT.HW	1232d	NA	NA	0%												
HWY.220.040	24	Approval of Design Exception Report	Fri 2/26/21	Fri 2/26/21	0d	0d	0d	MassDOT.HW	1232d	NA	NA	0%												
HWY.220.050	25	Approval of Design Exception Report by Chief Engine	Sun 3/28/21	Sun 3/28/21	0d	0d	0d	MassDOT.HW	1232d	NA	NA	0%												
HWY.230	26	Healthy Transportation Waiver	Mon 3/25/19	Sun 1/19/20	301d	301d	0d		0d	Mon 3/25/19	Sun 1/19/20	100%	Healthy Transportation Waiver											
HWY.303	32	Conduct Survey	Tue 11/17/20	Wed 1/27/21	72d	46.8d	25.2d		1142d	Tue 11/17/20	NA	65%	Conduct Survey											
HWY.303.020	33	Conduct Survey - Parking Lot / Off-site	Tue 11/17/20	Wed 1/27/21	72d	46.8d	25.2d	Consultants.DES	1142d	Tue 11/17/20	NA	65%												
HWY.250	34	Pre-25% Design	Sun 3/24/19	Tue 7/23/19	121d	121d	0d		0d	Sun 3/24/19	Tue 7/23/19	100%	Pre-25% Design											
HWY.300	39	25% Highway Design Submission	Wed 7/24/19	Wed 1/29/20	190d	190d	0d		0d	Wed 7/24/19	Wed 1/29/20	100%	25% Highway Design Submission											
HWY.350	50	Design Public Hearing	Tue 2/4/20	Sat 8/29/20	208d	208d	0d		0d	Tue 2/4/20	Sat 8/29/20	100%	Design Public Hearing											
HWY.400	54	75% Highway Design Submission	Tue 11/10/20	Wed 7/7/21	240d	21.18d	218.82d		107d	Tue 11/10/20	NA	9%	75% Highway Design Submission											
HWY.400.010	55	Prepare 75% Highway Design Submission	Tue 11/10/20	Thu 4/8/21	150d	22.5d	127.5d	Consultants.DES	5d	Tue 11/10/20	NA	15%												
HWY.400.020	56	Submit 75% Design Submission	Thu 4/8/21	Thu 4/8/21	0d	0d	0d	Consultants.DES	37d	NA	NA	0%	◆ Submit 75% Design Submission											
HWY.400.030	57	Prepare 75% Construction Contract Time Determination	Mon 4/19/21	Mon 5/3/21	15d	0d	15d	Consultants.Other	72d	NA	NA	0%												
HWY.400.040	58	Review 75% Highway Design Submission	Fri 4/9/21	Mon 6/7/21	60d	0d	60d	MassDOT.HW	37d	NA	NA	0%												
HWY.400.011	59	Prepare 75% Highway Design Submission Rev1	Mon 6/7/21	Mon 6/7/21	0d	0d	0d	Consultants.DES	37d	NA	NA	0%												
HWY.400.021	60	Submit 75% Highway Design Submission Rev1	Mon 6/7/21	Mon 6/7/21	0d	0d	0d	Consultants.DES	37d	NA	NA	0%												
HWY.400.041	61	Review 75% Highway Design Submission Rev1	Mon 6/7/21	Mon 6/7/21	0d	0d	0d	MassDOT.HW	37d	NA	NA	0%												
HWY.400.050	62	All Sections 75% Highway Design Comments sent to DE	Mon 6/7/21	Mon 6/7/21	0d	0d	0d	MassDOT.HW	37d	NA	NA	0%												
HWY.400.070	63	Prepare 75% Design Responses	Tue 6/8/21	Wed 7/7/21	30d	0d	30d	Consultants.DES	107d	NA	NA	0%												
HWY.400.080	64	Comment Resolution Meeting @75% (Full Team)	Wed 7/7/21	Wed 7/7/21	0d	0d	0d	MassDOT.PM	107d	NA	NA	0%												
HWY.450	65	100% Highway Design Submission	Tue 6/8/21	Mon 10/25/21	140d	0d	140d		37d	NA	NA	0%	100% Highway Design Submission											
HWY.450.010	66	Prepare 100% Highway Design Submission	Tue 6/8/21	Wed 9/15/21	100d	0d	100d	Consultants.DES	37d	NA	NA	0%												
HWY.450.020	67	Submit 100% Design Submission	Wed 9/15/21	Wed 9/15/21	0d	0d	0d	Consultants.DES	116d	NA	NA	0%	◆ Submit 100% Design Submission											
HWY.450.030	68	Finalize Construction Contract Time Determination	Sun 9/26/21	Sun 10/10/21	15d	0d	15d	Consultants.Other	121d	NA	NA	0%												
HWY.450.040	69	Review 100% Highway Design Submission	Thu 9/16/21	Fri 10/15/21	30d	0d	30d	MassDOT.HW	116d	NA	NA	0%												
HWY.450.011	70	Prepare 100% Highway Design Submission Rev1	Fri 10/15/21	Fri 10/15/21	0d	0d	0d	Consultants.DES	116d	NA	NA	0%												
HWY.450.021	71	Submit 100% Design Submission Rev1	Fri 10/15/21	Fri 10/15/21	0d	0d	0d	Consultants.DES	116d	NA	NA	0%												
HWY.450.041	72	Review 100% Highway Design Submission Rev1	Fri 10/15/21	Fri 10/15/21	0d	0d	0d	MassDOT.HW	116d	NA	NA	0%												
HWY.450.070	73	Prepare 100% Design Responses	Sat 10/16/21	Mon 10/25/21	10d	0d	10d	Consultants.DES	116d	NA	NA	0%												
HWY.450.080	74	Comment Resolution Meeting @100% (Full Team)	Mon 10/25/21	Mon 10/25/21	0d	0d	0d	MassDOT.PM	116d	NA	NA	0%												
HWY.450.100	75	Approval of 100% Highway Design Submission	Mon 10/25/21	Mon 10/25/21	0d	0d	0d	MassDOT.HW	116d	NA	NA	0%												
HWY.800	76	PS&E Submittal	Tue 10/26/21	Wed 12/15/21	51d	0d	51d		116d	NA	NA	0%	PS&E Submittal											
HWY.800.010	77	Prepare PS&E Submission	Tue 10/26/21	Wed 11/24/21	30d	0d	30d	Consultants.DES	116d	NA	NA	0%												
HWY.800.020	78	Submit PS&E Submission	Wed 11/24/21	Wed 11/24/21	0d	0d	0d	Consultants.DES	116d	NA	NA	0%	◆ Submit PS&E Submission											
HWY.800.040	79	Review PS&E Submission	Thu 11/25/21	Wed 12/1/21	7d	0d	7d	MassDOT.PM	116d	NA	NA	0%												
HWY.800.045	80	Peer Review of PS&E Submission (if applicable)	Thu 12/2/21	Wed 12/15/21	14d	0d	14d	Consultants.Other	116d	NA	NA	0%												

Task [Blue Bar] Milestone [Diamond] Summary [Arrow] Critical Path [Red Bar] Progress [Green Bar]

WBS	ID	Name	Start	Finish	Duration	Actual Duration	Remaining Duration	Responsibility	Total Slack	Act. Start	Act. Finish	% Complete	Timeline											
													1st Quarter Nov	3rd Quarter Jan	1st Quarter Mar	3rd Quarter May	1st Quarter Jul	3rd Quarter Sep	1st Quarter Nov	3rd Quarter Jan	1st Quarter Mar	3rd Quarter May	1st Quarter Jul	3rd Quarter Sep
HWY.800.100	81	Approval of PS&E Submission	Wed 12/15/21	Wed 12/15/21	0d	0d	0d	MassDOT.HW	116d	NA	NA	0%	◆ Approval of PS&E Submission											
HWY.800.110	82	Submit Mylars	Wed 12/15/21	Wed 12/15/21	0d	0d	0d	Consultants.DES	545d	NA	NA	0%	◆ Submit Mylars											
HWY.800.120	83	Highway Design Scope Complete	Wed 12/15/21	Wed 12/15/21	0d	0d	0d	MassDOT.PM	970d	NA	NA	0%	◆ Highway Design Scope Complete											
BRD	84	Highway/Bridge Design	Thu 1/28/21	Sun 6/6/21	130d	0d	130d		1162d	NA	NA	0%	Highway/Bridge Design											
BRD.600	85	Geotechnical Design	Thu 1/28/21	Sun 6/6/21	130d	0d	130d		1162d	NA	NA	0%	Geotechnical Design											
ENV	92	Environmental	Wed 1/2/19	Thu 11/4/21	1038d	411.77d	626.23d		157d	Wed 1/2/19	NA	40%	Environmental											
ENV.MS	93	Environmental Milestones	Fri 4/9/21	Thu 11/4/21	210d	0d	210d		157d	NA	NA	0%	Environmental Milestones											
ENV.MS.010	94	Wetland Permits Filed - NOI, Other	Wed 7/7/21	Wed 7/7/21	0d	0d	0d	MassDOT.ENV	277d	NA	NA	0%	◆ Wetland Permits Filed - NOI, Other											
ENV.MS.*	95	Submit Draft ENF	Fri 4/9/21	Fri 4/9/21	1d	0d	1d	Consultants.DES	215d	NA	NA	0%												
ENV.MS.*	96	Review ENF	Sat 4/10/21	Thu 7/8/21	90d	0d	90d	MassDOT.ENV	215d	NA	NA	0%												
ENV.MS.*	97	Revise ENF	Fri 7/9/21	Sat 8/7/21	30d	0d	30d	Consultants.DES	215d	NA	NA	0%												
ENV.MS.*	98	File ENF	Sun 8/8/21	Sun 8/8/21	1d	0d	1d	MassDOT.ENV	215d	NA	NA	0%												
ENV.MS.*	99	MEPA approval of ENF	Mon 8/9/21	Tue 9/7/21	30d	0d	30d	MassDOT.ENV	215d	NA	NA	0%												
ENV.MS.020	100	Issue Environmental Clearance	Thu 11/4/21	Thu 11/4/21	0d	0d	0d	MassDOT.ENV	157d	NA	NA	0%	◆ Issue Environmental Clearance											
ENV.151	101	25% Early Environmental Coordination	Wed 1/2/19	Fri 12/20/19	353d	353d	0d		0d	Wed 1/2/19	Fri 12/20/19	100%	25% Early Environmental Coordination											
ENV.152	106	State or Federal Historic Review	Thu 11/21/19	Fri 4/3/20	135d	135d	0d		0d	Thu 11/21/19	Fri 4/3/20	100%	State or Federal Historic Review											
ENV.157	112	NEPA-Categorical Exclusion (CE)	Fri 4/9/21	Mon 6/7/21	60d	0d	60d		35d	NA	NA	0%	NEPA-Categorical Exclusion (CE)											
ENV.157.010	113	Prepare Categorical Exclusion	Fri 4/9/21	Fri 4/23/21	15d	0d	15d	Consultants.DES	35d	NA	NA	0%												
ENV.157.020	114	Submit Categorical Exclusion	Fri 4/23/21	Fri 4/23/21	0d	0d	0d	Consultants.DES	35d	NA	NA	0%	◆ Submit Categorical Exclusion											
ENV.157.030	115	Review Categorical Exclusion	Sat 4/24/21	Sat 5/8/21	15d	0d	15d	MassDOT.ENV	35d	NA	NA	0%												
ENV.157.040	116	Review Categorical Exclusion by FHWA	Sun 5/9/21	Mon 6/7/21	30d	0d	30d	Agencies.FHWA	35d	NA	NA	0%												
ENV.157.050	117	Approve Categorical Exclusion	Mon 6/7/21	Mon 6/7/21	0d	0d	0d	MassDOT.ENV or Agencies.FHWA	35d	NA	NA	0%	◆ Approve Categorical Exclusion											
ENV.171	118	404 Permit - ACOE PGP/SV	Fri 7/31/20	Thu 11/4/21	462d	0d	462d		157d	NA	NA	0%	404 Permit - ACOE PGP/SV											
ENV.171.010	119	Prepare ACOE PGP/SV	Fri 7/31/20	Sat 8/29/20	30d	0d	30d	MassDOT.ENV	469d	NA	NA	0%												
ENV.171.020	120	File ACOE Permit Application	Wed 7/7/21	Wed 7/7/21	0d	0d	0d	MassDOT.ENV	157d	NA	NA	0%	◆ File ACOE Permit Application											
ENV.171.030	121	Agency Review ACOE Application	Thu 7/8/21	Thu 11/4/21	120d	0d	120d	Agencies.ACOE	157d	NA	NA	0%												
ENV.171.040	122	Approve ACOE PGP/SV	Thu 11/4/21	Thu 11/4/21	0d	0d	0d	Agencies.ACOE	157d	NA	NA	0%	◆ Approve ACOE PGP/SV											
ENV.173	123	De minimis 4(f) N/A	Tue 2/4/20	Tue 4/28/20	85d	85d	0d		0d	Tue 2/4/20	Tue 4/28/20	100%	De minimis 4(f) N/A											
ENV.182	131	Water Quality Certification	Fri 4/9/21	Sun 9/5/21	150d	0d	150d		187d	NA	NA	0%	Water Quality Certification											
ENV.182.010	132	Prepare Draft WQC	Fri 4/9/21	Sat 5/8/21	30d	0d	30d	Consultants.DES	187d	NA	NA	0%												
ENV.182.020	133	Submit Draft WQC	Sat 5/8/21	Sat 5/8/21	0d	0d	0d	Consultants.DES	187d	NA	NA	0%	◆ Submit Draft WQC											
ENV.182.030	134	Review Draft WQC	Sun 5/9/21	Mon 6/7/21	30d	0d	30d	MassDOT.ENV	187d	NA	NA	0%												
ENV.182.040	135	File WQC	Mon 6/7/21	Mon 6/7/21	0d	0d	0d	MassDOT.ENV	187d	NA	NA	0%	◆ File WQC											
ENV.182.050	136	Agency Review WQC	Tue 6/8/21	Sun 9/5/21	90d	0d	90d	Agencies.DEP	217d	NA	NA	0%												
ENV.182.060	137	Issue Water Quality Certification	Sun 9/5/21	Sun 9/5/21	0d	0d	0d	Agencies.DEP	217d	NA	NA	0%	◆ Issue Water Quality Certification											
ENV.185	138	Notice of Intent	Wed 12/30/20	Sat 10/16/21	291d	0d	291d		157d	NA	NA	0%	Notice of Intent											
ENV.185.010	139	Prepare Draft NOI	Wed 12/30/20	Thu 4/8/21	100d	0d	100d	Consultants.DES	157d	NA	NA	0%												
ENV.185.020	140	Submit Draft NOI	Thu 4/8/21	Thu 4/8/21	0d	0d	0d	Consultants.DES	157d	NA	NA	0%	◆ Submit Draft NOI											
ENV.185.030	141	Review Draft NOI	Fri 4/9/21	Wed 7/7/21	90d	0d	90d	MassDOT.ENV	157d	NA	NA	0%												
ENV.185.040	142	Municipality Review NOI	Thu 7/8/21	Fri 8/6/21	30d	0d	30d	Other.Municipality	176d	NA	NA	0%												
ENV.185.*	143	Revise Combined NOI based on Town/MassDOT Comments	Sat 8/7/21	Sun 9/5/21	30d	0d	30d		176d	NA	NA	0%												
ENV.185.*	144	Conservation Hearing	Mon 9/6/21	Sat 9/25/21	20d	0d	20d	Consultants.DES	176d	NA	NA	0%												
ENV.185.050	145	Issue Order of Conditions	Sun 9/26/21	Sat 10/16/21	21d	0d	21d	Other.Municipality	176d	NA	NA	0%												
ROW	146	Right of Way	Wed 7/24/19	Tue 4/5/22	987d	113.59d	873.41d		5d	Wed 7/24/19	NA	12%	Right of Way											
ROW.501	147	25% ROW Plans	Wed 7/24/19	Mon 2/3/20	195d	195d	0d		0d	Wed 7/24/19	Mon 2/3/20	100%	25% ROW Plans											
ROW.503	154	Preliminary Municipal ROW Plans	Fri 7/31/20	Tue 4/5/22	614d	0d	614d		5d	NA	NA	0%	Preliminary Municipal ROW Plans											
ROW.503.01	155	Municipal Review Process	Mon 2/8/21	Fri 11/12/21	278d	0d	278d		5d	NA	NA	0%	Municipal Review Process											
ROW.503.01.010	156	Prepare 75% ROW Plans	Mon 2/8/21	Thu 4/8/21	60d	0d	60d	Consultants.DES	5d	NA	NA	0%												
ROW.503.01.020	157	Submit 75% ROW Plans	Thu 4/8/21	Thu 4/8/21	0d	0d	0d	Consultants.DES	5d	NA	NA	0%	◆ Submit 75% ROW Plans											
ROW.503.01.030	158	Review 75% ROW Plans	Fri 4/9/21	Mon 6/7/21	60d	0d	60d	MassDOT.ROW	5d	NA	NA	0%												
ROW.503.01.011	159	Prepare 75% ROW Plans Rev1	Mon 6/7/21	Mon 6/7/21	0d	0d	0d	Consultants.DES	5d	NA	NA	0%	◆ Prepare 75% ROW Plans Rev1											
ROW.503.01.021	160	Submit 75% ROW Plans Rev1	Tue 6/8/21	Wed 7/7/21	30d	0d	30d	Consultants.DES	5d	NA	NA	0%												
ROW.503.01.031	161	Review 75% ROW Plans Rev1	Wed 7/7/21	Wed 7/7/21	0d	0d	0d	MassDOT.ROW	5d	NA	NA	0%	◆ Review 75% ROW Plans Rev1											
ROW.503.01.040	162	Approve 75% ROW Plans	Wed 7/7/21	Wed 7/7/21	0d	0d	0d	MassDOT.ROW	5d	NA	NA	0%	◆ Approve 75% ROW Plans											
ROW.503.01.012	163	Prepare 100% ROW Plans	Sun 7/18/21	Wed 9/15/21	60d	0d	60d	Consultants.DES	37d	NA	NA	0%												
ROW.503.01.022	164	Submit 100% ROW Plans	Wed 9/15/21	Wed 9/15/21	0d	0d	0d	Consultants.DES	37d	NA	NA	0%	◆ Submit 100% ROW Plans											
ROW.503.01.032	165	Review 100% ROW Plans	Thu 9/16/21	Fri 10/15/21	30d	0d	30d	MassDOT.ROW	37d	NA	NA	0%												


█ Task
 ◆ Milestone
 █ Summary
 ▶ Critical Path
 █ Progress

Massachusetts Department of Transportation

608164 - Town of Sudbury, MA - Bruce Freeman Rail Trail

UD PDS Schedule

WBS	ID	Name	Start	Finish	Duration	Actual Duration	Remaining Duration	Responsibility	Total Slack	Act. Start	Act. Finish	% Complete	Quarter																								
													1st Quarter	3rd Quarter	1st Quarter	3rd Quarter	1st Quarter	3rd Quarter	1st Quarter	3rd Quarter	1st Quarter	3rd Quarter	1st Quarter	3rd Quarter													
ROW.503.01.013	166	Prepare 100% ROW Plans Rev1	Sat 10/16/21	Fri 10/29/21	14d	0d	14d	Consultants.DES	37d	NA	NA	0%																									
ROW.503.01.023	167	Submit 100% ROW Plans Rev1	Fri 10/29/21	Fri 10/29/21	0d	0d	0d	Consultants.DES	37d	NA	NA	0%																									
ROW.503.01.033	168	Review 100% ROW Plans Rev1	Sat 10/30/21	Fri 11/12/21	14d	0d	14d	MassDOT.ROW	37d	NA	NA	0%																									
ROW.503.01.050	169	Approve 100% ROW Plans	Fri 11/12/21	Fri 11/12/21	0d	0d	0d	MassDOT.ROW	37d	NA	NA	0%																									
ROW.503.02	170	Municipal Acquisition Process	Fri 7/31/20	Tue 4/5/22	614d	0d	614d		5d	NA	NA	0%																									
ROW.503.02.010	171	Hold Town Meeting	Fri 7/31/20	Wed 5/26/21	300d	0d	300d	Other.Municipality	47d	NA	NA	0%																									
ROW.503.02.020	172	Perform Title Exams (All TPI)	Thu 7/8/21	Thu 8/26/21	50d	0d	50d	Other.Municipality	5d	NA	NA	0%																									
ROW.503.02.030	173	Contact Property Owners	Fri 8/27/21	Fri 10/15/21	50d	0d	50d	Other.Municipality	5d	NA	NA	0%																									
ROW.503.02.040	174	Perform Appraisals (All TPI)	Sat 10/16/21	Tue 12/14/21	60d	0d	60d	Other.Municipality	5d	NA	NA	0%																									
ROW.503.02.050	175	Prepare Layout Taking Plans & Instrument	Thu 7/8/21	Fri 8/6/21	30d	0d	30d	Consultants.DES	77d	NA	NA	0%																									
ROW.503.02.060	176	Submit Layout TPIs	Fri 8/6/21	Fri 8/6/21	0d	0d	0d	Consultants.DES	77d	NA	NA	0%																									
ROW.503.02.070	177	Review Layout TPIs	Sat 8/7/21	Fri 8/20/21	14d	0d	14d	and Other.Municipality	77d	NA	NA	0%																									
ROW.503.02.051	178	Prepare Layout Taking Plans & Instrument Rev1	Sat 8/21/21	Sun 9/19/21	30d	0d	30d	Consultants.DES	77d	NA	NA	0%																									
ROW.503.02.061	179	Submit Layout TPIs Rev 1	Sun 9/19/21	Sun 9/19/21	0d	0d	0d	Consultants.DES	77d	NA	NA	0%																									
ROW.503.02.071	180	Review Layout TPIs Rev 1	Mon 9/20/21	Sun 10/3/21	14d	0d	14d	and Other.Municipality	77d	NA	NA	0%																									
ROW.503.02.080	181	Approve Layout Taking Plans	Fri 11/12/21	Fri 11/12/21	0d	0d	0d	and Other.Municipality	37d	NA	NA	0%																									
ROW.503.02.151	182	Town / MassDOT RR Lease Agreement	Thu 7/8/21	Tue 10/5/21	90d	0d	90d		187d	NA	NA	0%																									
ROW.503.02.090	183	Offer & Negotiations	Wed 12/15/21	Sat 2/12/22	60d	0d	60d	Other.Municipality	5d	NA	NA	0%																									
ROW.503.02.100	184	Municipal Approval, Record & File	Sun 2/13/22	Mon 3/14/22	30d	0d	30d	Other.Municipality	5d	NA	NA	0%																									
ROW.503.02.110	185	Acquisitions Recorded & Filed	Mon 3/14/22	Mon 3/14/22	0d	0d	0d	Other.Municipality	5d	NA	NA	0%																									
ROW.503.02.120	186	Submit Community Compliance Package	Tue 3/15/22	Mon 3/21/22	7d	0d	7d	Other.Municipality	5d	NA	NA	0%																									
ROW.503.02.130	187	Review Community Compliance Package	Tue 3/22/22	Tue 4/5/22	15d	0d	15d	MassDOT.ROW	5d	NA	NA	0%																									
ROW.503.02.140	188	Pay Award of Damages	Tue 3/15/22	Sun 4/3/22	20d	0d	20d	Other.Municipality	7d	NA	NA	0%																									
ROW.503.02.150	189	Issue ROW Certificate	Tue 4/5/22	Tue 4/5/22	0d	0d	0d	MassDOT.PM	5d	NA	NA	0%																									
CSS	190	Construction Engineering	Sun 8/13/23	Sun 8/11/24	365d	0d	365d		0d	NA	NA	0%																									
CSS.900	191	Construction Support Services	Sun 8/13/23	Sun 8/11/24	365d	0d	365d		0d	NA	NA	0%																									
CSS.900.010	192	Construction Support Services	Sun 8/13/23	Sun 8/11/24	365d	0d	365d	Consultants.DES	0d	NA	NA	0%																									

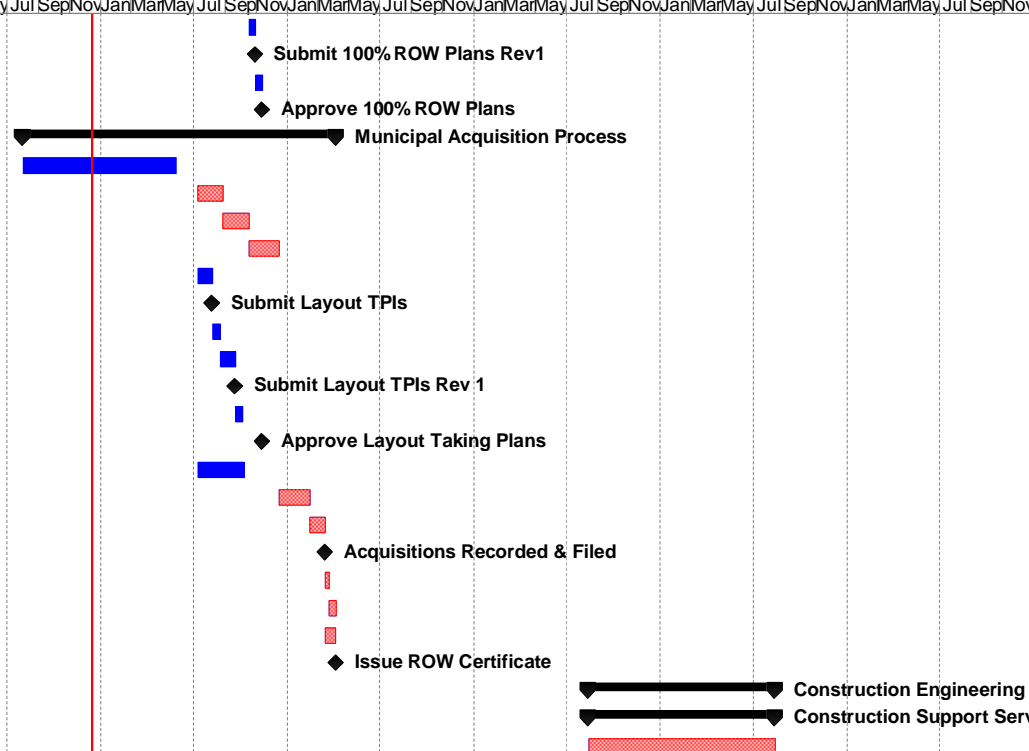

Task ■ Milestone ◆ Summary ▬ Critical Path ■ Progress ▬
